DKS Door Order Sheet

Fire Rated		
Std.	3 Hour (Standard)	90 minutes on 1100 and 9000
Extra Charge: 20, 45, 60, or 90 min. (Specify)		

Lock and Hinge Locations	
DKS	Standard
CU	Curries
CE	Ceco
REP	Old Republic
DE	Dean Steel, Mesker, New Republic
PIO	Pioneer

Series		Cores
1100	Corner Seam	Polystyrene
1300	Steel Stiffened (18 ga.)	Mineral wool
1600	16 ga. Flush	Polystyrene
1700	18 ga. 6 Panel	Polystyrene
1800	18 ga. Flush	Polystyrene
1900	18 ga. 2 Panel	Polystyrene
2000	18 ga. Flush	Honeycomb
6000	18 ga. Double Egress	Honeycomb
9000	18 ga. Temp Rise	Mineral/Pyrophobic

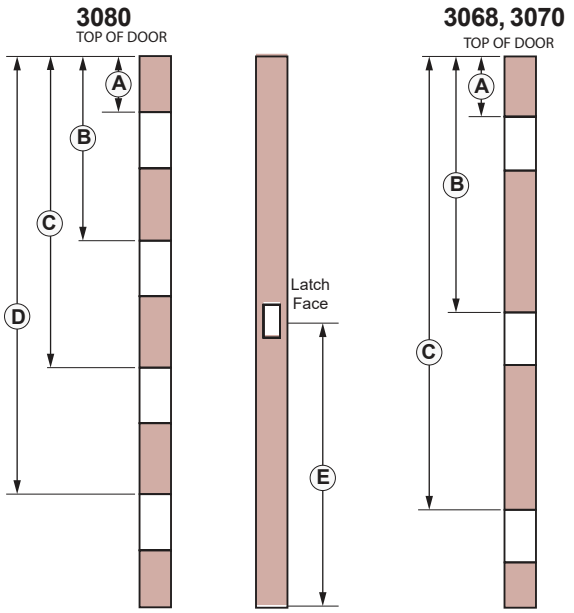

Hardware Prep	
C	161
MB	86
BR	Blank Rim Panic
SVR	Surf. Vert. Rod
IA	Fl. Blt. X ASA

Special Modifications		
LDMOD-9	Dead bolt prep (specify location)	
LDMOD-23	Peephole prep (specify location)	
LDMOD-11	Weld flat astragal (specify handing)	
	Door Cutout	
Cutout Size	Cutout Location	Fire Rated (Y/N)

DKS Standard Door Measurements					
	A	B	C	D	E
3068	7 3/8	37 5/16	67 1/4	-----	39 9/16
3070	7 3/8	39 5/16	71 1/4	-----	
3080	7 3/8	32 11/16	58	83 5/16	

Company Name :	PO #	Account # :	SO # :
Ordered By:	Ship To:		

	QTY	Series	Item/Door Number	Door Opening Size (in Feet) (W x H)		Vision Lite Opening Size (in Feet) (W x H)		Lock and Hinge Locations	Hardware Prep	Special Modification	Notes
1											
2											
3											
4											
5											
6											
7											
8											
9											
10											

DKS Frame Order Sheet

DKS Standard Frame Measurements					
	A	B	C	D	E
3068	7 1/2	37 7/16	67 3/8	-----	40 5/16
3070		39 7/16	71 3/8		
3080		32 13/16	58 1/8	83 7/16	

Strike and Hinge Locations	
DKS	Standard
CU	Curries
CE	Ceco
REP	Old Republic
DE	Dean Steel, Mesker, New Republic
PIO	Pioneer

Series	
M	Masonry (16 Gauge)
D	Drywall
EXP M	Expandable Masonry
EXP D	Expandable Drywall
DE	Double Egress
PIO	Masonry (14 Gauge)

Notes	
Fire Rating:	
Std	3 Hour = Masonry, Drywall = 90 Min.
Extra Charge: 20, 45, 60, or 90 Min. (Specify)	
Note: Standard Frame Type is Unequal Rabbet	

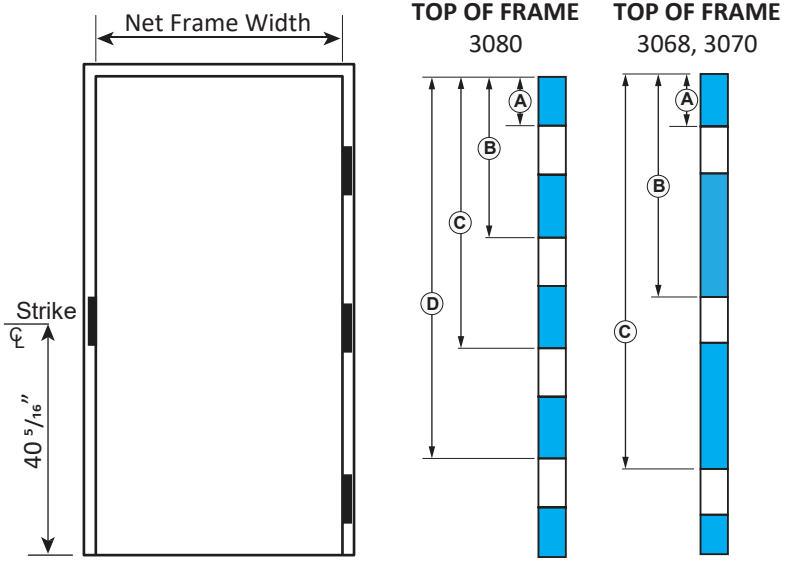

Handing	
LH	LH or RHR
RH	RH or LHR

Hardware Prep	
ASA	ASA 4 7/8" (Standard)
T	T-Strike
DS	Deadbolt Strike
RP	Rim Panic Reinf.
VRP	Vertical Rod Strike
FBF	Flush Bolt Strike
RA	Reg. Arm Closer Reinf.
PA	P. Arm Closer Reinf.
For more options see catalog pages LC3-LC4 in price sheet	

Anchors	
WS	Wood Stud
SS	Steel Stud
MAS01	Masonry Wire
SAC5	L-Strap
PDW	P&D Wood
PDM	P&D Masonry

Company Name:	PO #:	Account #:	SO #:
Ordered By:	Ship To:		

	QTY	Series	Item Number	Jamb Depth	Strike & Hinge Locations	Opening Size (in Feet) (W x H)		Handing	Welded Face (Y/N)	Closer Reinforcement	Anchor	Welded-Anchor (Y/N)	Hardware Prep	Notes
1														
2														
3														
4														
5														
6														
